

DESIGN							4/27/2017
Project No.	Project Description	Received	CDs/DDs Due	DM	PM	Budget (\$)	
31902	UCA 4100 Office Addition	6/24/2015	1/7/2016	SM/SB	JS	\$14,400	Hold
32324	HMU Finish Improvements	11/23/2015	5/5/2017	SB	JS	TBD	
32326	Bellamy Atrium Renovation Study	5/10/2016	10/26/2016	SM	GF	\$648,000	Hold
32435	CUP Main Office Interior Improvements	XXXXX	10/4/2016	EW/AW	JL	TBD	Hold
32453	UCA 1403 Office Modifications	6/27/2016		SM	BC	\$30,000	Bid/Permitting
1531718	Pres' House Carport Canopy Extension Studies	2/27/2015	6/04/2015	SM	JST	TBD	Hold
1439731	Sandels Deans Ste Renovation DD & Est	4/22/2014	9/10/2014	SM	TBD	TBD	Hold
1700066	MMA Phase II: Ste. 125 Renovation	9/16/2015	5/12/2017	SM	JS	300,000	
1700090	Kursteiner 200 ASF Entry Replacement(89)	02/12/17	4/12/2017	AG	JS	37,600	Bid/Permitting
1700092	Housewright 200 ASF Entry Replacement (54)	2/12/17	4/12/2017	AG	JS	37,600	Bid/Permitting
PN TBD	Thrasher 1130 Office Addition DD & Estimate	1/7/2015	2/26/2015	AG	TBD	TBD	Hold
PN TBD	Bio-1 3rd Floor Lab Shell Prep	9/17/2013	8/13 ?	AG	BQ	TBD	Hold
1700043	WFSU TV Studio Life Safety Improvements	5/20/2016	9/12/2016	AG	BC	TBD	Pending
1700098	CML Fence Replacement (89)	2/12/2017	6/13/2017	AG	JS	\$8,200	
REQ100119	CCFT Door Security Improvements	8/1/2016	1/31/2017	AG	BC	TBD	Pending
1700111	Keen 619 Renovation	2/12/2017	5/10/2017	AG	MJS	TBD	
1700117	Shores C&I Card Swipe Additions	2/12/2017	6/9/2017	AG	JS	\$13,200	
1700200	Multidisciplinary Center Relocation	3/31/2017	7/21/2017	SB	DL	\$1,000,000	
1700244	Law Rotunda 107 Conversion to Multipurpose Rm.	2/12/2017	6/30/2017	SB	BC	TBD	
1700243	BKR 318 Conversion to Recording Studio	2/7/2017	5/10/2017	SM	BC	TBD	
1700204	UCA 1400 Reception Renovations	10/13/2016	3/15/2017	SB	BC	TBD	
1700237	MagLab Short Stay Facility Project Name	2/10/2017	7/7/2017	SM	MJS	\$1,000,000	
1700325	Sliger/ Johnson: Anthropology Relocation	4/4/2017		AG	DL	\$200,000	
1700253	UCD 2216 Digital Media Ste Study/Est (226)	2/16/2017	6/16/2017	JC	BC	TBD	
1700255	Howser Sports Medicine 115 Interior Improvements (115)	2/10/2017	5/19/2017	SB	BC	\$25,000	
1700261	Dirac RR Renovation	2/12/2017	5/2/2017	SB	BC	\$200,000	
1700273	Longmire Renovation of Dean's Ste(72)	5/24/2016	8/1/2017	SM	JS	\$351,500	Bid/Permitting
1700267	UCC 1st Floor Lobby Improvements	3/29/2016	5/12/2017	JC	BC	TBD	
PN TBD	Diffenbaugh ste 001A DD & Est	4/24/2015	8/4/2015	SB	TBD	\$132,400	Hold
1700180	Bellamy 402/404 Renov (08)	2/10/2017	4/19/2017	AG	BC	\$330,200	
1700159	EHS Hazardous Wastw Bldg Safety Improvements	2/2/2017	5/24/2017	SM	GF	TBD	
1700075	UCA Suites 1200 & 1500 Finish Improvements	5/4/2016	6/20/2016	SB	JS	TBD	Hold
1700196	DSC 32000 Cabinet Addition	2/14/2017	3/9/2017	AG	JS	TBD	Bid/Permitting
1700095	Degraff West Generator Screen Wall	12/1/2016	4/24/2017	AG	JL	TBD	
WO TBD	UCB University Ctr. Club Blinds Est	XXXXX	05/04/16	SB	TBD	TBD	Hold
WO TBD	UCA 4th Floor Public Lobby Improvements Est	11/18/2014	9/11/2015	EB	TBD	TBD	Hold
WO TBD	Housewright Exhibit Room Renovation	6/18/2014	8/6/2014	EB	TBD	TBD	Hold
REQ100115	Wellness 4114 Office Additions	9/23/16	4/26/17	SM	JS	TBD	
1700210	RBB 229 Conversion to Seminar Rm (52)	11/18/16	4/20/17	SM	BQ	125,000	
REQ100219	WES ste 216	10/4/16	11/14/16	SB	NA	TBD	Hold
1700117	Kursteiner/ Opperman Stage Floor Replacement	11/10/16	5/24/17	AG	JS	TBD	
1700156	Dodd Hall Transformer Screen Wall	10/25/16	1/24/17	SM	JL	TBD	Hold
1700073	Tanner Hall Conference Rm Modification	7/26/16	11/22/16	SB	JS	TBD	Hold
17000148	UCA 6317 Office Modifications	2/12/2017		JC	BC	51,000	
1700182	Moran Institute Tallahassee F&E Selections	1/6/17	2/14/2017	SB	BQ	450,000	
PN TBD	BRF Exit Door Modification	2/12/2017	5/31/17	JC	MJS	3,600	
WO TBD	Opperman Music Hall Exterior Terrace Est	11/16/11	TBD	EB	TBD	TBD	Hold

DM= Design Manager	AW=Andy Welch	SC= Substantial Completion
GMP = Guaranteed Maximum Price	SM=Sean Mitchell	PM=Project Manager
CD=Construction Documents	AG=Allen Golden	
DD= Design Development	JC: Jazmine Coachman	
F&E PM (Project Manager) Abbreviations		
BA=Brad Adams	RI=Russell Taunilas	
BO= Bill Quarles	JS=Justin Shafer	
BL=Bill Lamb	RH=Robert Harris	
GF=Gary Feldman	KB=Kim Ball	
JST=Jim Stanley	BK=Bill King	

MINOR PROJECT STATUS REPORT - CONSTRUCTION 4/27/2017

Project No.	Project Description	Received	SC Date	DM	PM	Budget (\$)	Status
32196	Strozier Annex Interior Improvements	8/18/2015	6/11/2016	SB	BC	\$226,700	FC Pending
32219	Kursteiner North Door Replacement	8/27/2012	TBD	AW	JS	\$73,000	In Progress
32228	Film School Door Replacements	1/6/2016	TBD	AG	BC	\$5,900	In Progress
32251	Strozier Annex 2nd Floor Interior Finish Improvements	TBD	1/12/2017	SB	BC	\$1,440,000	In Progress
1700076	Rovetta Digital Signs	8/19/2016	TBD	AW	BC	TBD	In Progress
1700088	WES 424C Modification (01)	9/12/16	4/04/17	AW	BC	\$19,900	FC Pending
REQ100319	Moran Institute Jacksonville Office F&E	TBD	4/26/17	SB	BQ	TBD	In Progress
REQ100047	Strozier Security Area Seating < Fixture Addition(134)	1/27/16	7/19/16	SB	KS	\$8,700	In Progress

Key

DM= Design Manager
 GMP = Guaranteed Maximum Price
 PM=Project Manager
 CD= Construction Documents
 SC= Substantial Completion
 TBD= To Be Determined
 FC=Final Completion


FSU PM (Project Manager) Abbreviations

GF= Gary Feldman GM=Gary Metcalf
 RT= Russell Taunitas MS=Marvin Simmons
 BQ= Biff Quarles BK=Bill King
 BL= Bill Lamb

FSU DM (Design Manager) Abbreviations

AW= Andy Welch SM= Sean Mitchell
 AG=Allan Golden

Active Projects Design Schedule

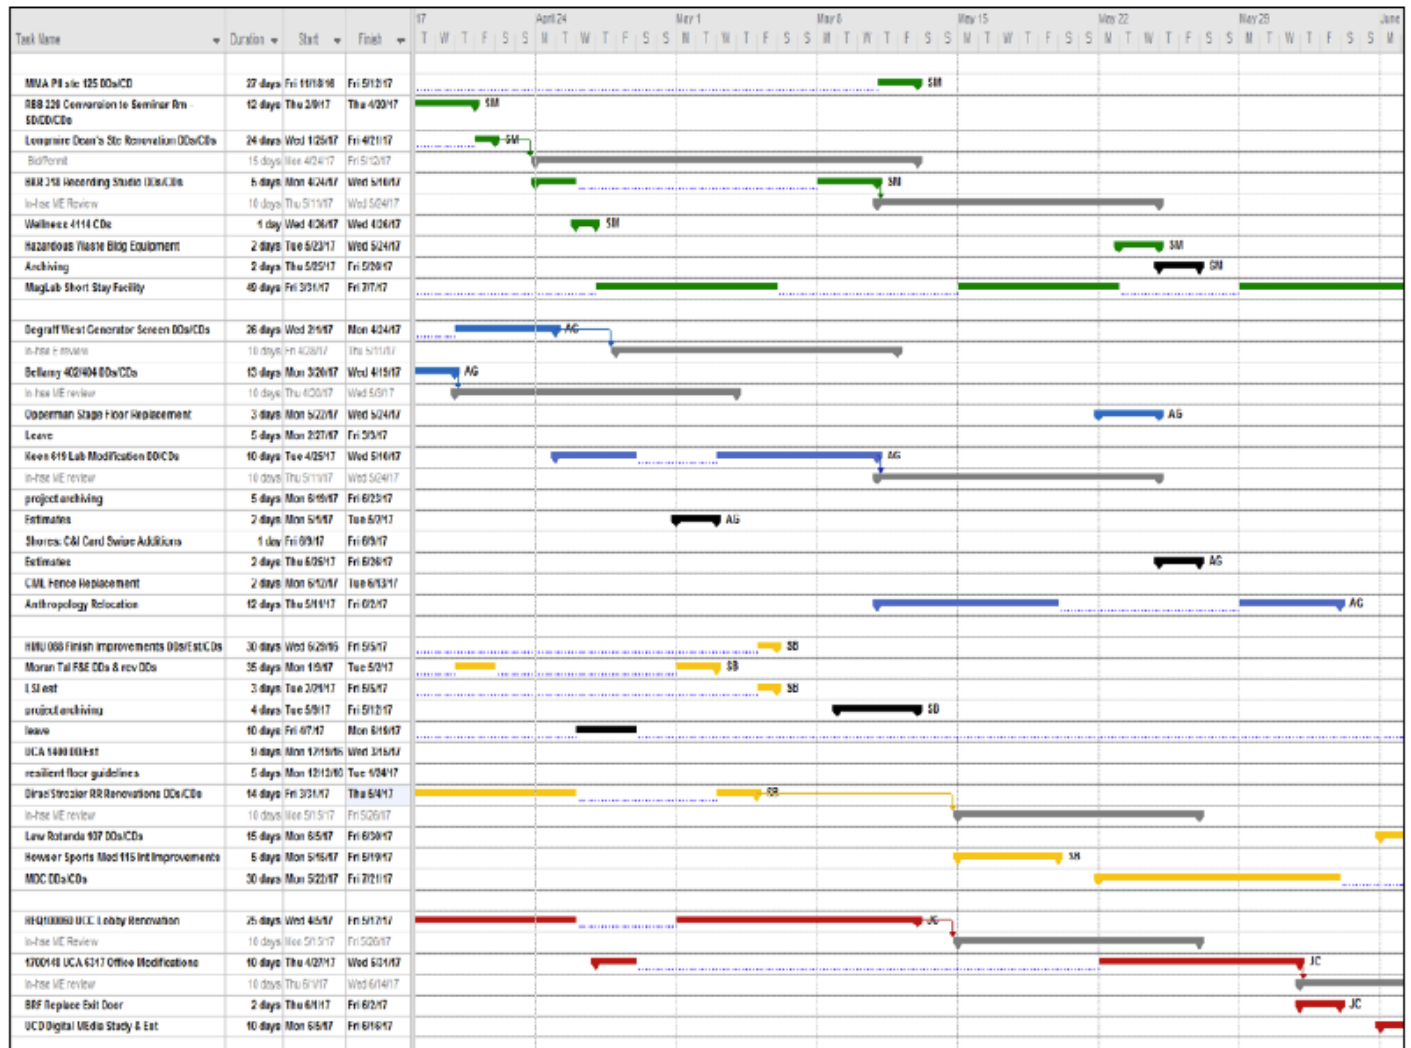

Extended Project Schedule

Task Name	Duration	Start	Finish	Feb	Mar	1st Quarter		May	Jun	2nd Quarter	
						Apr			Jul	Aug	
Longmire Dean's Ste Renovation DDs/CDs	24 days	Wed 1/25/17	Fri 4/21/17	[Task Bar]							
Bid/Permit	15 days	Mon 4/24/17	Fri 5/12/17					[Task Bar]			
GMP	5 days	Mon 5/15/17	Fri 5/19/17					[Task Bar]			
CA (3 mos)	55 days	Mon 5/22/17	Fri 8/4/17						[Task Bar]		
BKR 318 Recording Studio DDs/CDs	5 days	Mon 4/24/17	Wed 5/10/17					[Task Bar]			
In-hse ME Review	10 days	Thu 5/11/17	Wed 5/24/17					[Task Bar]			
Bid/Permit	15 days	Thu 5/25/17	Wed 6/14/17					[Task Bar]			
GMP TBV	5 days	Thu 6/15/17	Wed 6/21/17					[Task Bar]			
CA (2 mos)	45 days	Thu 6/22/17	Wed 8/23/17						[Task Bar]		
Degraff West Generator Screen DDs/CDs	26 days	Wed 2/1/17	Mon 4/24/17	[Task Bar]							
In-hse E review	10 days	Fri 4/28/17	Thu 5/11/17					[Task Bar]			
Bid/Permit	10 days	Fri 5/12/17	Thu 5/25/17					[Task Bar]			
GMP	5 days	Fri 5/26/17	Thu 6/1/17					[Task Bar]			
CA (2.5 mos)	56 days	Fri 6/2/17	Fri 8/18/17						[Task Bar]		
Bellamy 402/404 DDs/CDs	13 days	Mon 3/20/17	Wed 4/19/17		[Task Bar]						
In-hse ME review	10 days	Thu 4/20/17	Wed 5/3/17					[Task Bar]			
Bid/Permit	10 days	Thu 5/4/17	Wed 5/17/17					[Task Bar]			
GMP	5 days	Thu 5/18/17	Wed 5/24/17					[Task Bar]			
CA (2.5 mos)	56 days	Thu 5/25/17	Thu 8/10/17						[Task Bar]		
Keen 619 Lab Modification DD/CDs	10 days	Tue 4/25/17	Wed 5/10/17					[Task Bar]			
In-hse ME review	10 days	Thu 5/11/17	Wed 5/24/17					[Task Bar]			
Bid/Permit	10 days	Thu 5/25/17	Wed 6/7/17					[Task Bar]			
CA (2 mos)	45 days	Thu 6/8/17	Wed 8/9/17						[Task Bar]		
Dirac/Strozier RR Renovations DDs/CDs	14 days	Fri 3/31/17	Thu 5/4/17		[Task Bar]						
In-hse ME review	10 days	Mon 5/15/17	Fri 5/26/17					[Task Bar]			
Bid/Permit	10 days	Mon 5/29/17	Fri 6/9/17					[Task Bar]			
CA (2 mos)	45 days	Mon 6/12/17	Fri 8/11/17						[Task Bar]		
REQ100060 UCC Lobby Renovation	25 days	Wed 4/5/17	Fri 5/12/17		[Task Bar]						
In-hse ME Review	10 days	Mon 5/15/17	Fri 5/26/17					[Task Bar]			
Bid/Permit	10 days	Mon 5/15/17	Fri 5/26/17					[Task Bar]			
GMP	5 days	Mon 5/29/17	Fri 6/2/17					[Task Bar]			
CA (2 mos)	45 days	Mon 6/5/17	Fri 8/4/17						[Task Bar]		
1700146 UCA 6317 Office Modifications	10 days	Thu 4/27/17	Wed 5/31/17		[Task Bar]						
In-hse ME review	10 days	Thu 6/1/17	Wed 6/14/17					[Task Bar]			
Bid/Permit	10 days	Thu 6/15/17	Wed 6/28/17					[Task Bar]			
CA (1.5 mos)	34 days	Thu 6/29/17	Tue 8/15/17						[Task Bar]		
