

MINOR PROJECT STATUS REPORT - CONSTRUCTION 8/30/2017


Project No.	Project Description	Received	SC Date	DM	PM	Budget (\$)	Status
32219	Kursteiner North Door Replacement	8/27/2012	5/16/2017	EB/AW	JS	\$73,000	FC Pending
32228	Film School Door R Film School Door Replacements	1/6/2016	TBD	AG	BC	\$5,900	In Progress
32251	Strozier Annex 2nd Floor Interior Finish Improvements	TBD	1/12/2017	SB	BC	\$1,440,000	FC Pending
1700076	Rovetta Digital Signage	8/19/2016	8/23/2017	AW	BC	\$37,500	FC Pending
1700090	Kursteiner 200 ASF Entry Replacement(89)	02/12/17	TBD	AW	JS	\$37,600	In Progress
1700095	Degraff West Generator Screen Wall	12/1/2016	10/30/2017	AG	JL	TBD	In Progress
1700098	CML Fence Replacement (89)	2/12/2017	6/19/2017	AG	JS	\$8,200	In Progress
1700117	Opperman Stage Floor Replacement	11/10/16	8/25/2017	AG	JS	TBD	In Progress
1700148	UCA 6317 Office Modifications	2/12/2017	9/01/2017	AW	BC	51,000	In Progress
1700092	Housewright 200 A; Housewright 200 ASF Entry Replacement (54)	2/12/17	TBD	AW	JS	37,600	In Progress
1700210	RBB 229 Conversion to Seminar Rm (52)	11/18/16	08/31/17	SM	KM	125,000	In Progress
1700243	BKR 318 Conversion to Recording Studio	02/07/17	TBD	SM	BC	\$137,500	FC Pending
1700267	UCC 1st Floor Lobby Improvements	3/29/2016	8/25/2017	AW	BC/KB	\$208,300	In Progress
1700273	Longmire Renovation of Dean's Ste(72)	5/24/2016	TBD	SM	JS	\$439,900	FC Pending
1700180	BELLAMY 402/404 Renov (08)	2/10/17	9/29/17	AG	BC	241,300	In Progress
1700264	BRF EXIT DOOR MBRF Exit Door Modification	2/12/17	TBD	AW	MJS	3,600	In Progress

Key	
DM= Design Manager	
GMP = Guaranteed Maximum Price	
PM=Project Manager	
CD= Construction Documents	
SC= Substantial Completion	
TBD= To Be Determined	
FC=Final Completion	
FSU PM (Project Manager) Abbreviations	
GF= Gary Feldman	GM=Gary Metcalf
RT= Russell Taunitas	MS=Marvin Simmons
BQ= Biff Quarles	BK=Bill King
BL= Bill Lamb	
FSU DM (Design Manager) Abbreviations	
AW= Andy Welch	SM= Sean Mitchell
AG=Allan Golden	

DESIGN							8/30/2017
Project No.	Project Description	Received	CDs/DDs Due	DM	PM	Budget (\$)	
31902	UCA 4100 Office Addition	6/24/2015	1/7/2016	SM/SB	JS	\$14,400	Hold
32324	HMU Finish Improvements	11/23/2015	6/12/2017	SB	JS	\$40,000	Bid/Permitting
1700361	Bellamy Atrium Renovation Study	5/10/2016	12/22/2017	SM	GF	\$600,000	
32435	CUP Main Office Interior Improvements	XXXXX	10/4/2016	EB/AW	JL	TBD	Hold
1531718	Pres' House Carport Canopy Extension Studies	2/27/2015	6/04/2015	SM	JST	TBD	Hold
1439731	Sandels Deans Ste Renovation DD & Est	4/22/2014	9/10/2014	SM	TBD	TBD	Hold
1700066	MMA Phase II: Ste. 125 Renovation	9/16/2015	8/1/2017	SM	JS	300,000	
PN TBD	Thrasher 1130 Office Addition DD & Estimate	1/7/2015	2/26/2015	AG	TBD	TBD	Hold
PN TBD	Bio-1 3rd Floor Lab Shell Prep	9/17/2013	8/13 ?	AG	BQ	TBD	Hold
1700043	WFSU TV Studio Life Safety Improvements	5/20/2016	7/31/2017	AG	BC	TBD	Bid/Permitting
REQ100119	CCFT Door Security Improvements	8/1/2016	1/31/2017	AG	BC	TBD	Pending
1700111	Keen 619 Renovation	2/12/2017		AG	GF	\$95,400	Bid/Permitting
1700193	SHAW rm 0131 Conversion to LAB room	7/25/2017		SM	MJS	TBD	Pending
1700241	Hoffman Third Floor ADA			AG	GF	TBD	Bid/Permitting
1700244	Law Rotunda 107 Conversion to Multipurpose Rm.	2/12/2017	9/1/2017	AG	BC	TBD	
1700200	MDC F&E	7/12/2017	1/26/2018	SB	DL	TBD	
1700204	UCA 1400 Reception Renovations	10/13/2016	7/6/2017	SB	BC	TBD	Pending
1700237	MagLab Short Stay Facility Project Name	2/10/2017	10/27/2017	SM	MJS	\$1,000,000	
1700253	UCD 2216 Digital Media Ste Study/Est (226)	2/16/2017	6/23/2017	JC	BC	TBD	Pending
1700255	Howser Sports Medicine 115 Interior Improvements (115)	2/10/2017	9/21/2017	SB	BC	\$25,000	
1700261	Dirac RR Renovation	2/12/2017	9/6/2017	SB	BC	\$200,000	
1700270	UCC 2304 Conference RM Renovation (225)	4/13/2017	9/15/2017	SB	BQ	TBD	
1700267	UCC 1st Floor Lobby Improvements	3/29/2016	8/22/2017	JC	BC	TBD	Bid/Permitting
PN TBD	Diffenbaugh ste 001A DD & Est	4/24/2015	8/4/2015	SB	TBD	\$132,400	Hold
1700159	EHS Hazardous Wastw Bldg Safety Improvements	2/2/2017	8/25/2017	SM	GF	\$49,000	Bid/Permitting
1700075	UCA Suites 1200 & 1500 Finish Improvements	5/4/2016	6/20/2016	SB	JS	TBD	Hold
WO TBD	UCB University Ctr. Club Blinds Est	XXXXX	05/04/16	SB	TBD	TBD	Hold
WO TBD	UCA 4th Floor Public Lobby Improvements Est	11/18/2014	9/11/2015	EB	TBD	TBD	Hold
WO TBD	Housewright Exhibit Room Renovation	6/18/2014	8/6/2014	EB	TBD	TBD	Hold
REQ100219	WES ste 216	10/4/16	11/14/16	SB	NA	TBD	Hold
1700156	Dodd Hall Transformer Screen Wall	10/25/16	1/24/17	SM	JL	TBD	Hold
1700177	UCA 3504 PN TBD (223)	06/01/17	8/30/2017	SM	BC	66,100	Pending
1700073	Tanner Hall Conference Rm Modification	7/26/16	11/22/16	SB	JS	TBD	Hold
1700182	Moran Institute Tallahassee F&E Selections	1/6/17	8/15/2017	SB	BQ	450,000	
1700302	Thrasher ste 2140 Modification	3/16/17	9/08/2017	JC	BQ	TBD	
1700338	UCA 5523 Conversion into offices (225)	4/13/17	8/30/2017	JC	BC	TBD	
1700363	Opperman Music Hall Exterior Terrace Est	11/16/11	11/17/2017	AG	GF	TBD	

DM= Design Manager	AW=Andy Welch	SC= Substantial Completion
GMP = Guaranteed Maximum Price	SM=Sean Mitchell	PM=Project Manager
CD=Construction Documents	AG=Allen Golden	
DD= Design Development		
F&E PM (Project Manager) Abbreviations		
BA=Brad Adams	RI=Russell Taunilas	
BQ= Biff Quarles	JS=Justin Shafer	
BL=Bill Lamb	RH=Robert Harris	
GF=Gary Feldman	KB=Kim Ball	
JST=Jim Stanley	BK=Bill King	

Active Project Schedule

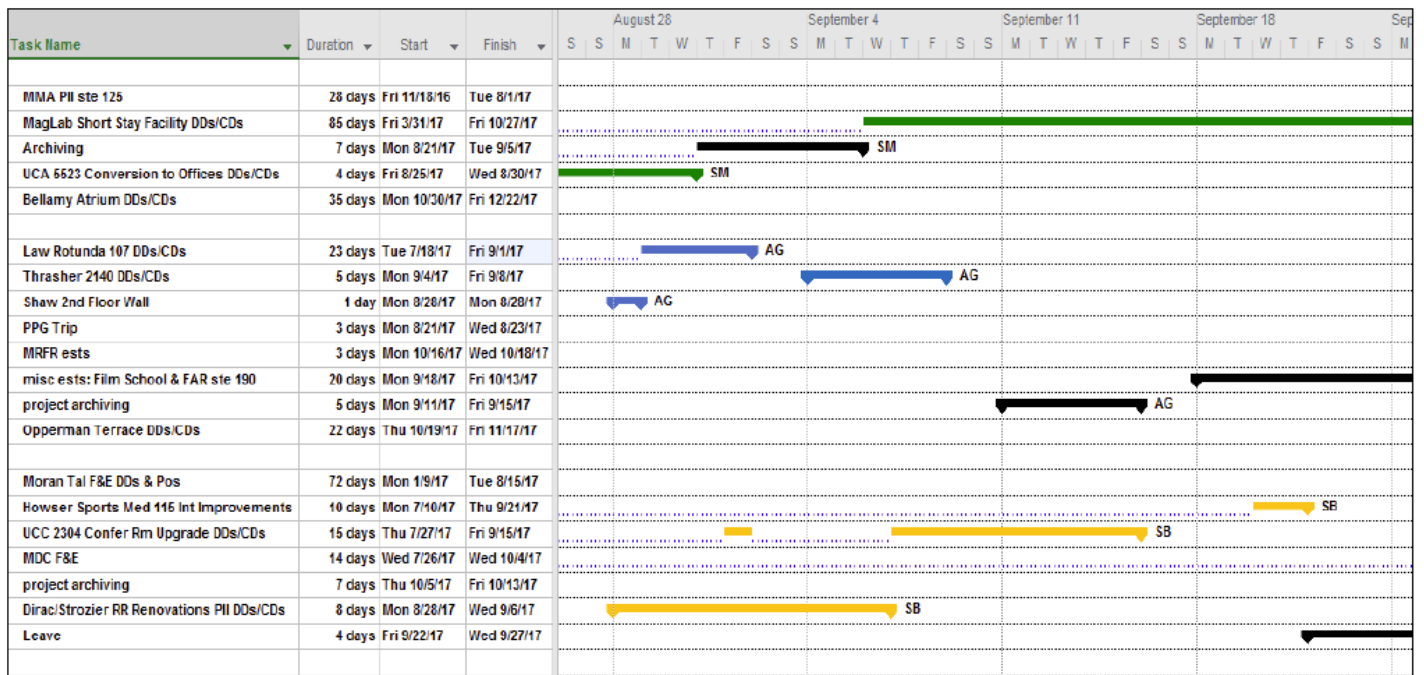

Extended Schedules

